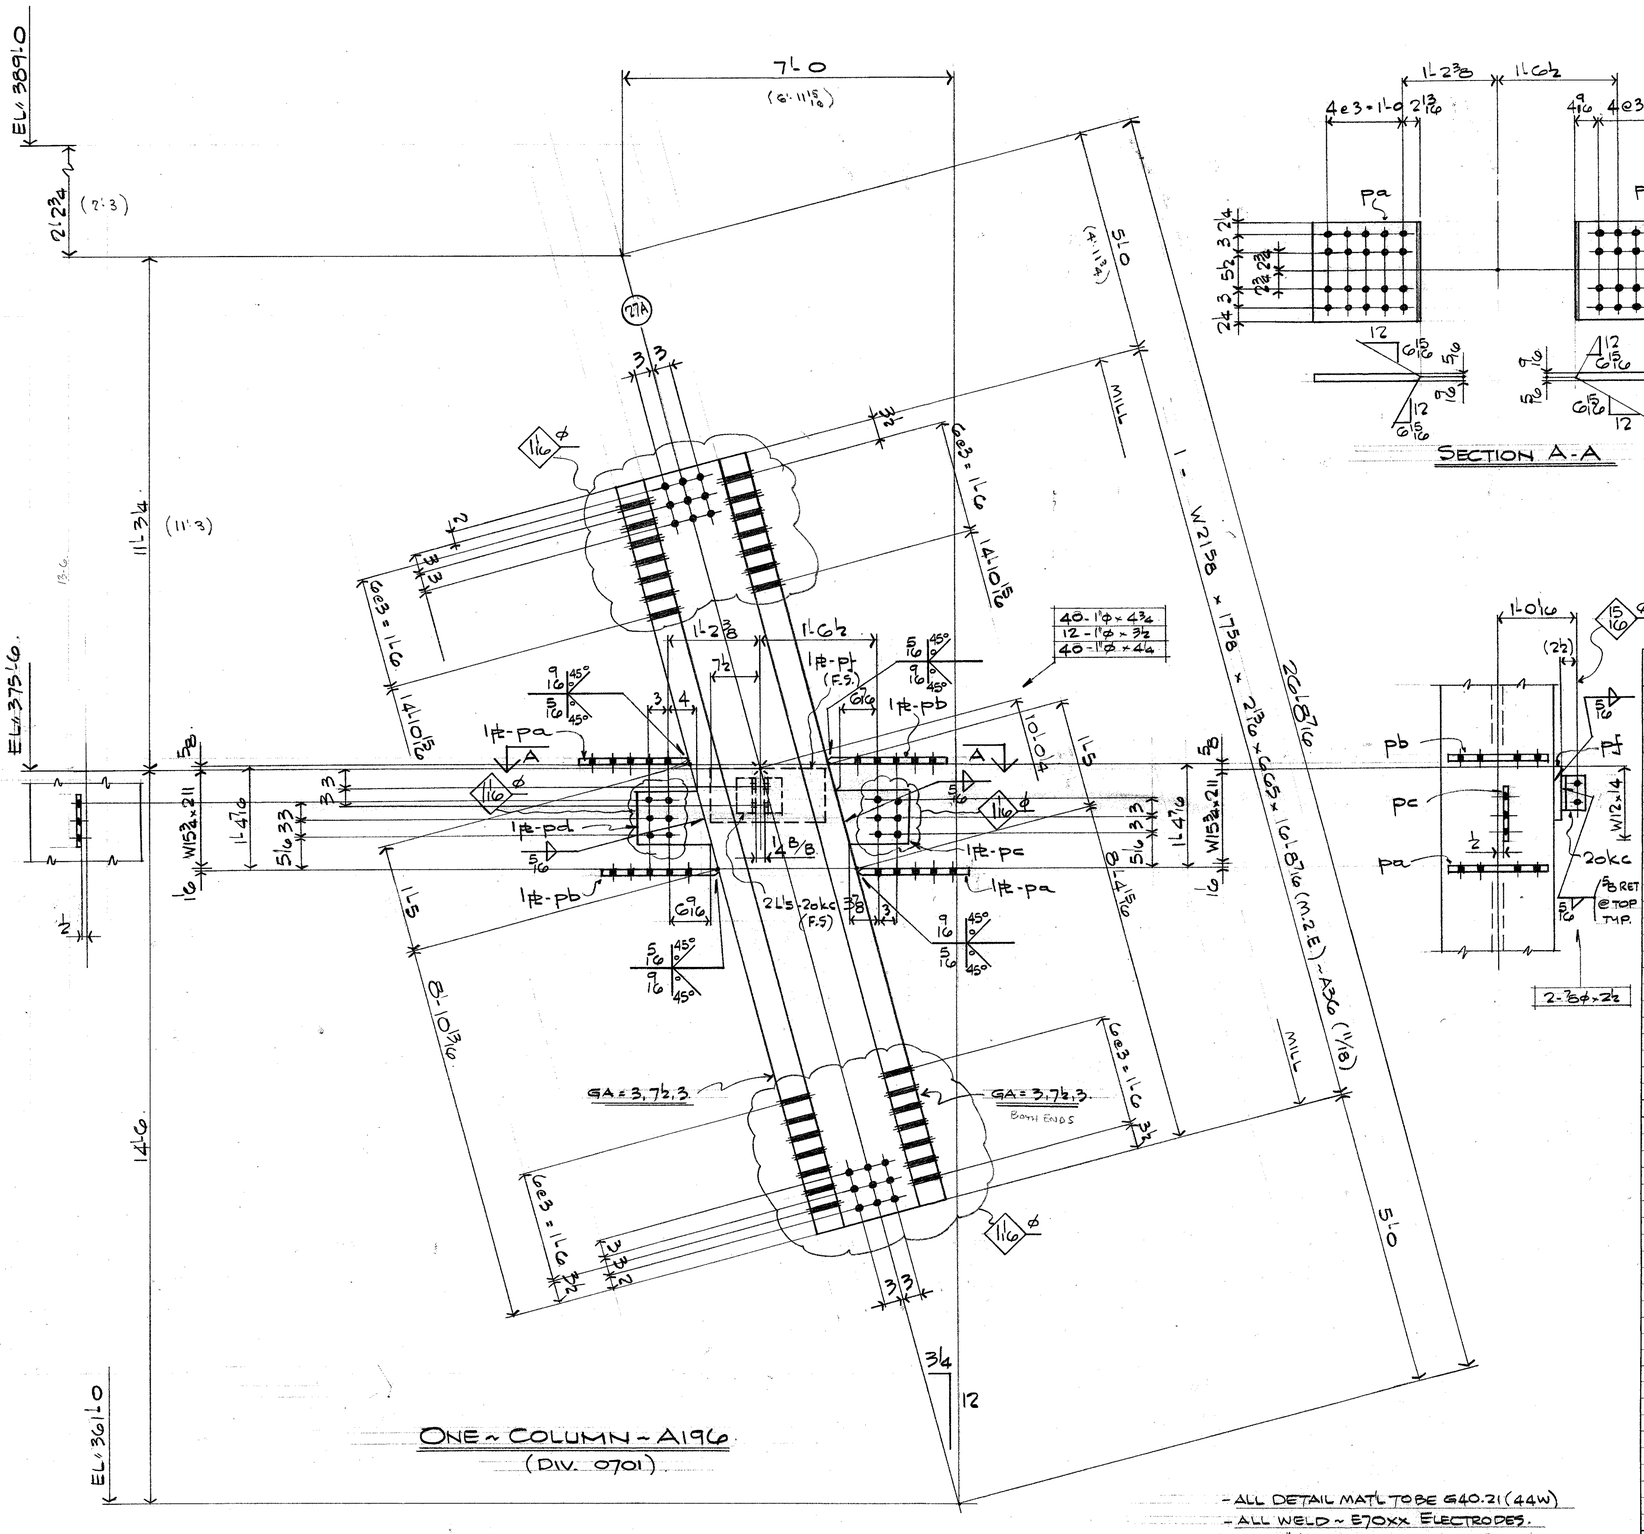


FIELD BOLT SUMMARY.

2 - 7/8ø A325 × 2½
12 - 1"ø A490 × 3½
40 - 〃 × 4½
40 - 〃 × 4¾
92 - EXTRA WASH (1"ø A490)

BILL OF MATERIAL

LINE	COST	COMMX SHIP DIVN.	PIECE MARKS MAIN MAT'L.	PIECE MARKS DETAIL MAT'L.	NO. OF PIECES	MATERIAL DESCRIPTION PL	WIDTH Inch	WIDTH 16th	X PLATE ONLY	THK. In.	THK. 16th	GRADE CODE	DSOR	FINISHED LENGTH Feet	FINISHED LENGTH In.	FINISHED LENGTH 16th	PAGE	LINE	REMARKS
01					Fool														
02																			
03				PA	2	PL	16	0	x	1	0	44W		1	5	0			
04				PB	2	〃	16	0	x	1	0	〃		1	6	12			
05				PC	1	〃	9	8	x	0	8	〃		1	0	4			
06				PD	1	〃	9	8	x	0	8	〃		1	0	4			
07				PF	1	〃	9	0	x	0	12	〃		1	6	8			
08																			
09				20kc	2	L	4×3×3/8					44W		0	5	8			
10																			
11					1	FL	5/16							5	10	0			
12					1	〃	6 9/16							5	4	0			
13					1	〃	6 9/16							5	4	0			
14																			
15																			
16	0701	A196			1	W	14×66#							16	8	7	11	18	M2E COL.
17																			
18																			
19																			
20																			
21																			
22																			
23																			
24																			
25																			
26			TOTAL		14				TOTAL					34					1 OF 1

IMPERIAL

REV.		DATE	BY
	1	DATE	BY
	2	DATE	BY
	3	DATE	BY

SPEC. A36 4/N
HOLES 13/16ø 4/N
FINISH —

FRANKEL STEEL LIMITED
220 ATTWELL DRIVE, UNIT 1, REXDALE, ONTARIO M9W 5B2

MADE		DATE	SQUAD
27	JS	MAR'85	FR
CHK'D. 28	MK	DATE APR 25	

PROJECT: 7 WORLD TRADE CENTRE
DETAIL: COL (27A) ~ (4TH LIFT).

CONTRACT 84-15
DWG.No. 196

- ALL DETAIL MATL TO BE G40.21(44W)
- ALL WELD ~ E70xx ELECTRODES.
- ALL 1"øA490 BOLTS TO HAVE 2 WASH.

ONE ~ COLUMN ~ A196
(DIV. 0701)
